경영회의 보고서

(2014년 01월)

2014.01.08

경영지원팀


목차


1. 전월지시사항
2. 공장전체 매출/부가가치/인원 현황
2-1. 주요 고객사 차량 및 가동계획
2-2. Chassis부문 운영 현황
1) 제품군별 매출 및 부가가치 현황
2) 라인 및 인력운영 현황
3) 생산성 현황
2-3. Seat 운영 현황
1) 제품군별 매출 및 부가가치 현황
2) 라인 및 인력운영 현황
3) 생산성 현황
3. 신규 Porject 진행 및 투자비 현황
3-1. 샤시사업본부 신규 Project 진행현황
3-2. 샤시사업본부 투자비 진행현황
3-3. 해외법인 선투자비 현황
3-4. 시트사업본부 신규 Project 진행 현황
3-5. 시트사업본부 투자비 진행현황
4. TCR2013 원가절감 현황
5. 2013년 고객사 차량판매 실적 현황
6. 사장님 말씀

1. 전월 지시사항

구분	지시 및 보완사항	지정부서	일정	추진실적 및 현황	추진부서	일정	진도	비고

2. 매출 / 부가가치 / 인원현황

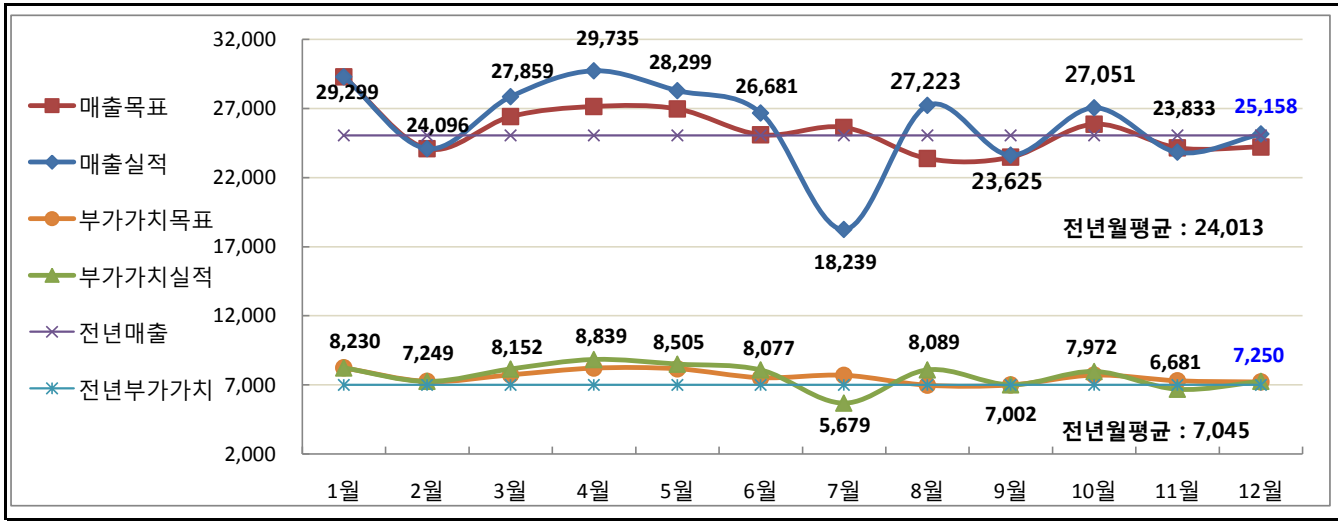

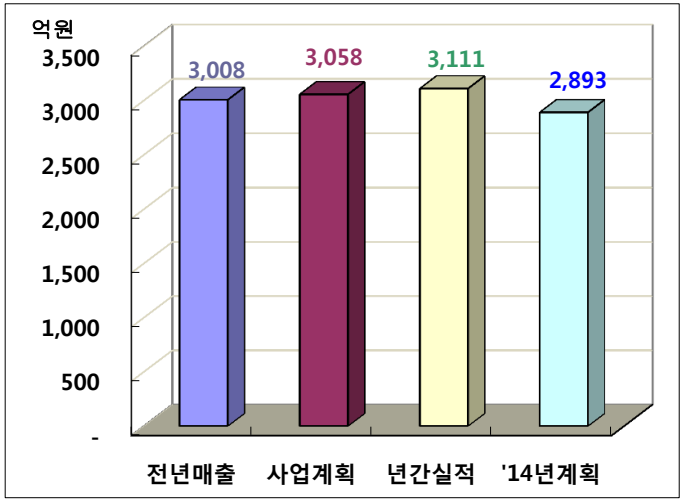


구분		2012년 월평균	2013년 1월	2월	3월	4월	5월	6월	7월	8월	9월	10월	11월	12월	합계	2014년 01월
매출 (백만원)	목표	26,300	29,299	24,096	26,420	27,149	26,974	25,100	25,640	23,381	23,483	25,871	24,158	24,221	**305,793**	23,215
	실적	25,065	29,299	24,096	27,859	29,735	28,299	26,681	18,239	27,223	23,625	27,051	23,833	25,158	**311,099**	(22,207)
	%	95%	100%	100%	105%	110%	105%	106%	71%	116%	101%	105%	99%	104%	**102%**	(96%)
부가 가치 (백만원)	목표	7,439	8,231	7,249	7,727	8,214	8,164	7,520	7,697	6,976	6,997	7,707	7,298	7,207	**90,987**	6,548
	실적	7,008	8,230	7,249	8,152	8,839	8,505	8,077	5,679	8,089	7,002	7,972	6,681	7,250	**91,725**	(6,360)
	%	94%	100%	100%	105%	108%	104%	107%	74%	116%	100%	103%	92%	101%	**101%**	(97%)
인원 현황 (명)	계획	551	550	551	562	562	564	564	564	564	564	564	564	564	**561**	536
	실적	551	550	551	549	551	549	545	544	544	537	538	533	534	**544**	(531)
	%	100%	100%	100%	98%	98%	97%	97%	96%	96%	95%	95%	95%	95%	**97%**	(99%)
인당 매출액 (백만원/명)	계획	47.8	53.3	43.7	47.0	48.3	47.8	44.5	45.5	41.5	41.6	45.9	42.8	42.9	**545**	43.3
	실적	45.5	53.3	43.7	50.7	54.0	51.5	49.0	33.5	50.0	44.0	50.3	44.7	47.1	**572**	(41.8)
	%	95%	100%	100%	108%	112%	108%	110%	74%	121%	106%	110%	104%	110%	**105%**	(97%)
인당 부가가치 (백만원/명)	계획	13.5	15.0	13.2	13.7	14.6	14.5	13.3	13.6	12.4	12.4	13.7	12.9	12.8	**162**	12.2
	실적	12.7	15.0	13.2	14.8	16.0	15.5	14.8	10.4	14.9	13.0	14.8	12.5	13.6	**169**	(12.0)
	%	94%	100%	100%	108%	110%	107%	111%	77%	120%	105%	108%	97%	106%	**104%**	(98%)


2-1. 주요 고객사 차량 및 가동계획

고객사		12월 실적				14년 01월 계획								14년 02월 전망			
		가동일	차량(대)		Total	가동일		차량(대)				Total		가동일	차량(대)		Total
								OEM		KD							
			OEM	KD			전월 대비	수량	전월 대비	수량	전월 대비	수량	전월 대비		OEM	KD	
부평#1	T250	**30**	720	7,950	**8,670**	**26**	87%	582	81%	9,706	122%	**10,288**	119%	**25**	1,079	6,702	**7,781**
	T300		3,213	-	**3,213**			2,468	77%	-		**2,468**	77%		1,821	-	**1,821**
	GSUV		23,060	-	**23,060**			19,840	86%	-		**19,840**	86%		18,640	-	**18,640**
부평#2	VS/V300	**21**	3,033	-	**3,033**	**16**	76%	2,240	74%	-		**2,240**	74%	**13**	1,860	-	**1,860**
	C140		5,700	810	**6,510**			5,590	98%	-		**5,590**	86%		4,500	-	**4,500**
군산	J200	**15**	1,512	7,616	**9,128**	**9**	60%	240	16%	3,200	42%	**3,440**	38%	**9**	-	3,600	**3,600**
	J300		7,352	6,855	**14,207**			6,380	87%	12,606	184%	**18,986**	134%		6,630	10,602	**17,232**
SYMC	A150	**21**	1,461	-	**1,461**	**20**	95%	1,320	90%	-		**1,320**	90%	**20**	1,250	-	**1,250**
RSM	L38/43/47	**17**	5,193	-	**5,193**	**18**	106%	6,353	122%	-		**6,353**	122%	**15**	5,034	-	**5,034**

2-2. 샤시부문 운영 현황

2-2-1. 매출 및 부가가치 현황

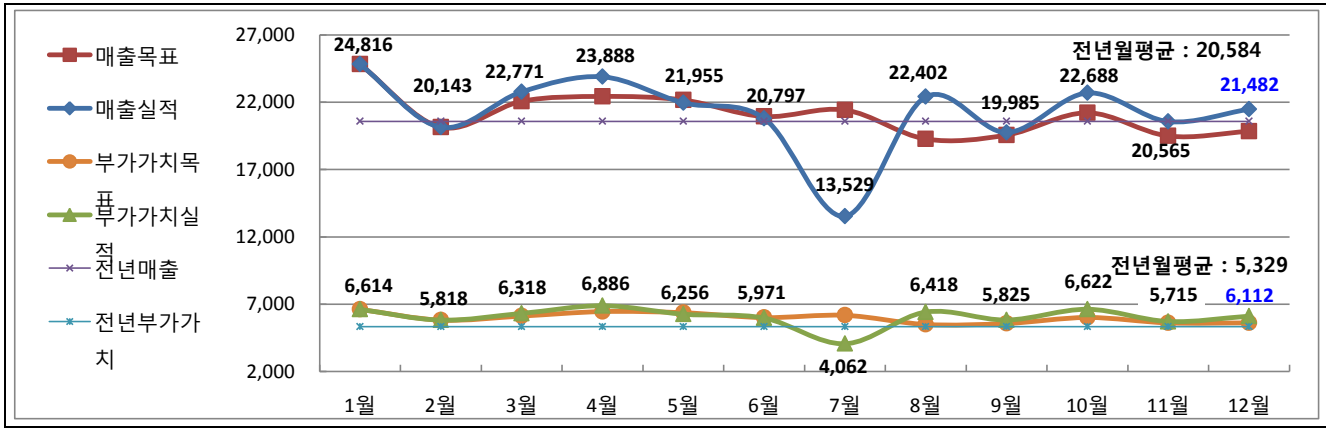

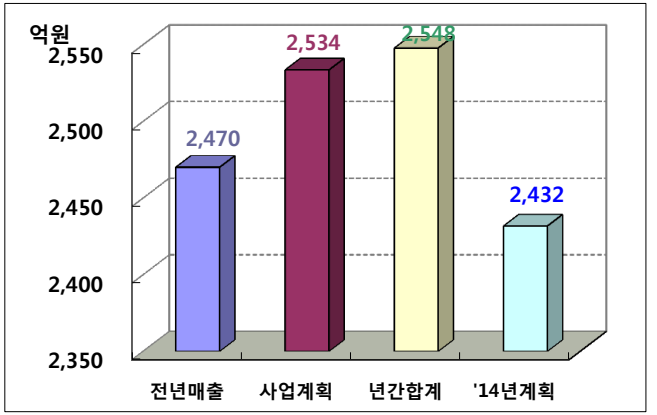

구분			2012년 월평균	2013년 1월	2월	3월	4월	5월	6월	7월	8월	9월	10월	11월	12월	합계	2014년 01월
매출	Wheel	계획	2,962	3,205	2,879	2,584	2,634	2,599	2,451	2,636	2,525	2,500	2,717	2,503	2,352	**31,586**	2,059
		실적	2,841	3,205	2,879	2,824	2,912	2,990	2,419	1,810	2,550	2,198	2,009	1,912	2,340	**30,048**	(1,965)
	Chassis	계획	18,412	21,189	16,897	19,012	19,307	19,102	18,050	18,346	16,324	16,696	18,049	16,537	17,078	**216,586**	17,296
		실적	17,290	21,189	16,897	19,513	20,483	18,483	17,922	11,481	19,337	17,159	20,195	18,258	18,729	**219,646**	(16,493)
	Module	계획	478	422	367	474	487	462	436	443	421	366	447	451	409	**5,185**	380
		실적	453	422	367	434	493	483	456	237	515	394	483	395	413	**5,091**	(370)
샤시사업본부Total		**계획**	**21,851**	**24,816**	**20,143**	**22,070**	**22,428**	**22,164**	**20,937**	**21,425**	**19,269**	**19,562**	**21,213**	**19,492**	**19,839**	**253,358**	**19,735**
		실적	**20,584**	**24,816**	**20,143**	**22,771**	**23,888**	**21,955**	**20,797**	**13,529**	**22,402**	**19,751**	**22,688**	**20,565**	**21,482**	**254,786**	**(18,828)**
		%	**94%**	**100%**	**100%**	**103%**	**107%**	**99%**	**99%**	**63%**	**116%**	**101%**	**107%**	**106%**	**108%**	**101%**	**(95%)**
부가가치	Wheel	계획	916	1,050	1,121	958	997	975	914	1,019	954	939	1,022	932	886	**11,766**	763
		실적	877	1,050	1,121	1,053	1,092	1,064	883	708	908	831	726	718	916	**11,069**	(770)
	Chassis	계획	4,326	5,142	4,330	4,687	4,968	4,931	4,656	4,712	4,120	4,262	4,544	4,228	4,318	**54,898**	4,383
		실적	3,999	5,142	4,330	4,832	5,301	4,709	4,632	3,117	4,995	4,601	5,413	4,602	4,782	**56,456**	(4,211)
	Module	계획	478	422	367	474	487	462	436	443	421	366	447	451	409	**5,185**	380
		실적	453	422	367	434	493	483	456	237	515	394	483	395	413	**5,092**	(370)
샤시사업본부Total		**계획**	**5,719**	**6,615**	**5,818**	**6,119**	**6,452**	**6,368**	**6,005**	**6,174**	**5,495**	**5,567**	**6,012**	**5,610**	**5,613**	**71,848**	**5,526**
		실적	**5,329**	**6,614**	**5,818**	**6,318**	**6,886**	**6,256**	**5,971**	**4,062**	**6,418**	**5,825**	**6,622**	**5,715**	**6,112**	**72,617**	**(5,351)**
		%	**93%**	**100%**	**100%**	**103%**	**107%**	**98%**	**99%**	**66%**	**117%**	**105%**	**110%**	**102%**	**109%**	**101%**	**(97%)**


2-2. 샤시부문 운영 현황

2-2-2. 라인 및 인력 운영 현황

라인별		12월 실적 인원	1월 계획					2월 전망			비 고 (충원 및 인력 운영 계획)
			인원	전월대비 증감		Shift	조업일수	인원	Shift	조업일수	
				인원	증감율						
Wheel	Disc	56	56	0	0%	1Shift	22	56	1Shift	21	
	Rim Ass'y#1					1Shift	22		1Shift	21	
	Rim Ass'y#2					1Shift	22		1Shift	21	
	ED					1Shift	22		1Shift	21	
Longi / Stamping		74	73	-1	-1%	2Shift	22	73	2Shift	21	중국 연태공장 1명 파견
C/MBR	GSUV	104	106	2	2%	2Shift	22	106	2Shift	21	
	J200					1Shift	22		1Shift	21	
	J300					2Shift	22		2Shift	21	
	C140					2Shift	22		2Shift	21	
C/ARM		18	18	0	0%	1 or 2Shift	22	18	1 or 2Shift	21	
E/D		18	18	0	0%	2Shift	22	18	2Shift	21	
직접 소계		**270**	**271**	**1**	**0%**			**271**			
	품질	33	33	0	0%			33			
	물류	33	33	0	0%			33			
	보전	15	15	0	0%			15			
간접 소계		**81**	**81**	**0**	**0%**			**81**			
합계		**351**	**352**	**1**	**0%**			**352**			

2-2. 샤시부문 운영 현황


2-2-3. 생산성 현황-Wheel

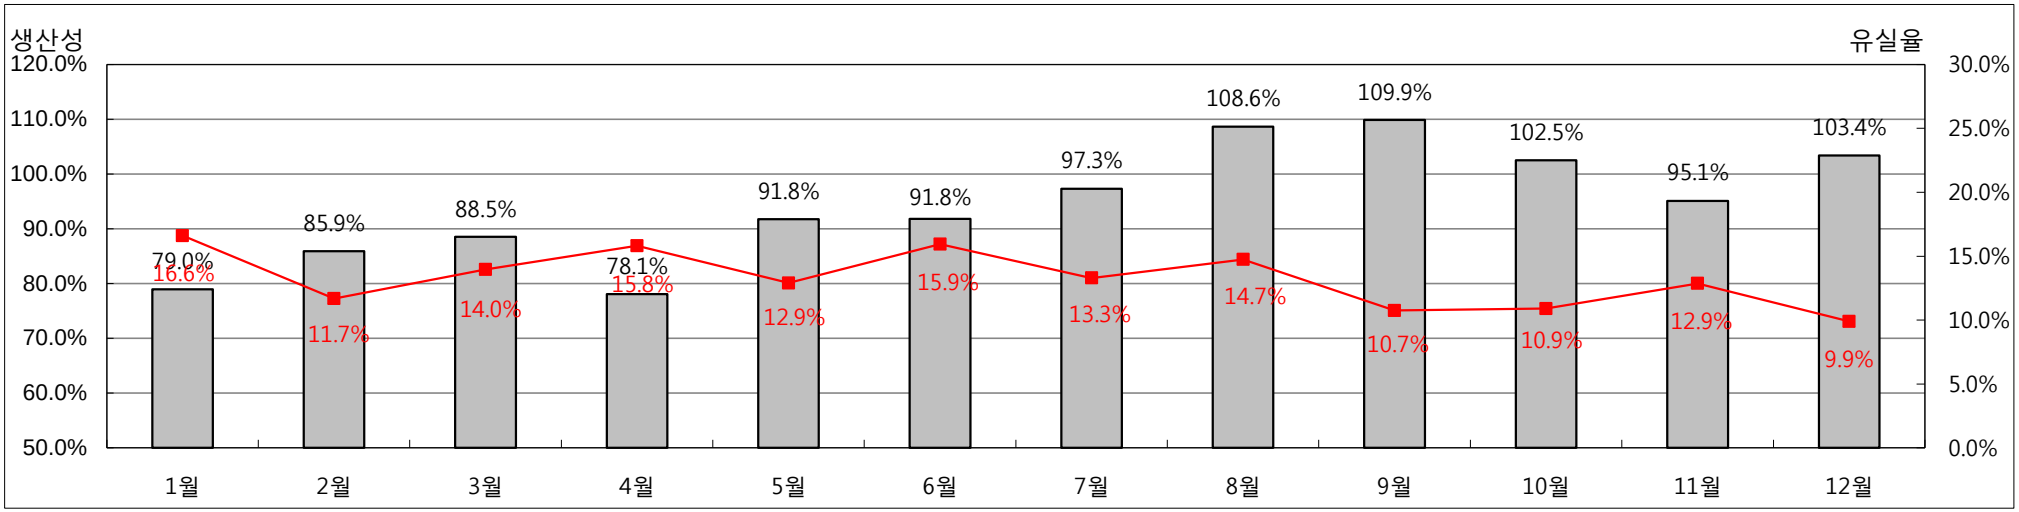

구분	CY2012 실적	CY2013												
		1월	2월	3월	4월	5월	6월	7월	8월	9월	10월	11월	12월	TOTAL
투입공수	116,735	12,015	9,593	11,009	10,659	9,263	8,565	6,325	6,828	6,262	6,750	6,468	7,109	100,846
유실공수	15,480	1,995	1,120	1,537	1,686	1,195	1,365	840	1,007	673	736	832	703	13,690
작업공수	101,255	10,020	8,473	9,471	8,973	8,068	7,199	5,484	5,821	5,589	6,014	5,636	6,406	87,156
표준공수	103,945	9,488	8,239	9,745	8,323	8,501	7,865	6,155	7,418	6,880	6,920	6,152	7,350	93,036
생산성(%)	89.0%	79.0%	85.9%	88.5%	78.1%	91.8%	91.8%	97.3%	108.6%	109.9%	102.5%	95.1%	103.4%	92.3%
성과율(%)	102.7%	94.7%	97.2%	102.9%	92.8%	105.4%	109.2%	112.2%	127.4%	123.1%	115.1%	109.1%	114.7%	106.7%
유실율(%)	13.3%	16.6%	11.7%	14.0%	15.8%	12.9%	15.9%	13.3%	14.7%	10.7%	10.9%	12.9%	9.9%	13.6%
유실금액(백만원)	279	36	20	28	30	22	25	15	18	12	13	15	13	246
인당 OT	**3.3**	**4.3**	**4.0**	**4.5**	**3.4**	**3.9**	**4.6**	**2.9**	**4.2**	**3.8**	**3.1**	**2.2**	**2.6**	**3.7**
주 유실원인		금형교환 품질조정 설비고장	금형교환 설비고장 품질조정	금형교환 설비고장 품질조정	금형교환 품질조정 설비고장	금형교환 품질조정 설비고장	금형교환 품질조정 설비고장	금형교환 품질조정 설비고장	금형교환 품질조정 설비고장	금형교환 설비고장 품질조정	금형교환 품질조정 설비고장	금형교환 설비고장 품질조정	금형교환 품질조정 설비고장	

2-2. 샤시부문 운영 현황


2-2-3. 생산성 현황-Chassis

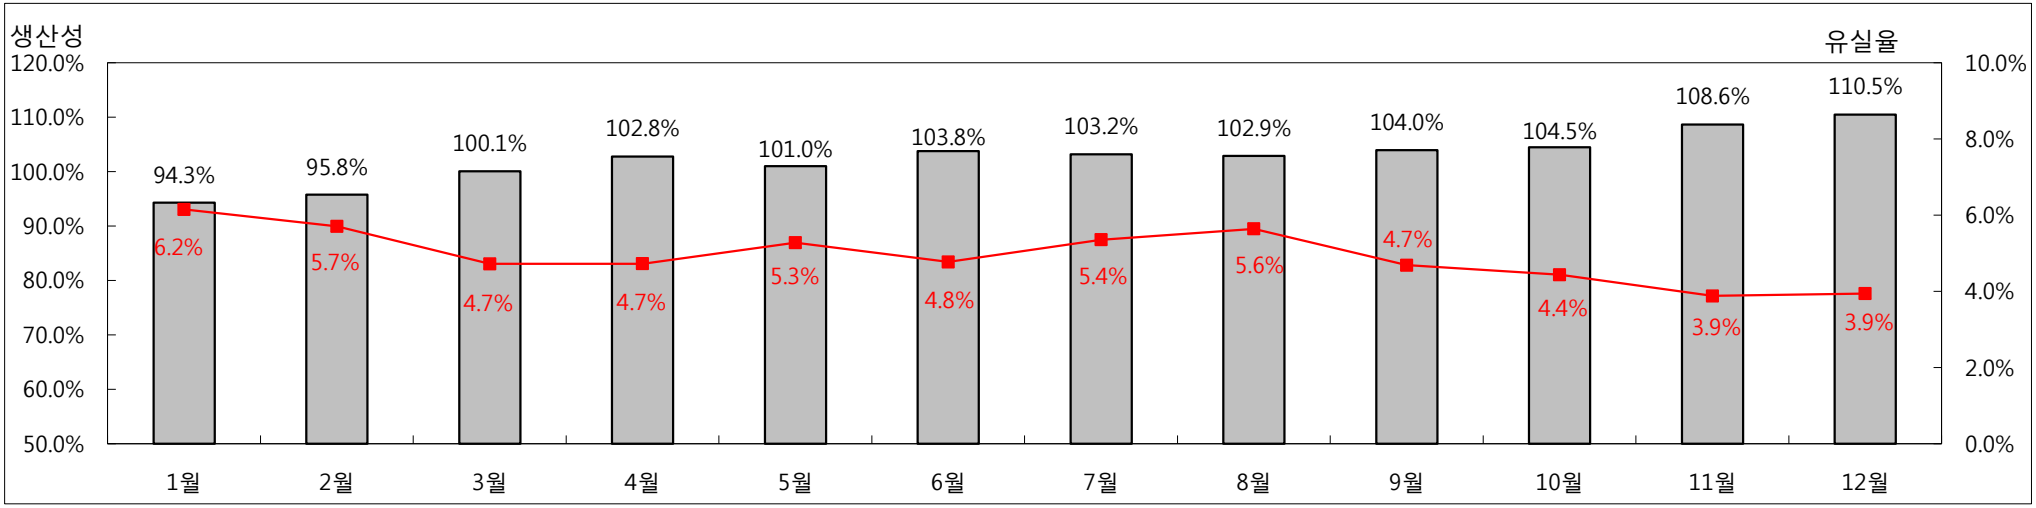


구분	CY2012 실적	CY2013												
		1월	2월	3월	4월	5월	6월	7월	8월	9월	10월	11월	12월	TOTAL
투입공수	272,537	27,663	25,030	28,485	24,914	30,575	28,379	18,216	29,450	27,420	29,923	26,790	29,200	326,045
유실공수	11,387	1,702	1,428	1,346	1,178	1,615	1,355	976	1,662	1,285	1,327	1,039	1,152	16,064
작업공수	261,162	25,961	23,602	27,139	23,736	28,960	27,024	17,240	27,789	26,134	28,596	25,750	28,049	309,981
표준공수	277,485	26,086	23,967	28,501	25,602	30,882	29,455	18,802	30,295	28,510	31,260	29,105	32,266	334,732
생산성(%)	101.8%	94.3%	95.8%	100.1%	102.8%	101.0%	103.8%	103.2%	102.9%	104.0%	104.5%	108.6%	110.5%	102.7%
성과율(%)	106.2%	100.5%	101.5%	105.0%	107.9%	106.6%	109.0%	109.1%	109.0%	109.1%	109.3%	113.0%	115.0%	108.0%
유실율(%)	4.2%	6.2%	5.7%	4.7%	4.7%	5.3%	4.8%	5.4%	5.6%	4.7%	4.4%	3.9%	3.9%	4.9%
유실금액(백만원)	205	31	26	24	21	29	24	18	30	23	24	19	21	289
인당 OT	**2.8**	**2.7**	**3.6**	**3.8**	**3.1**	**3.4**	**3.9**	**0.3**	**4.4**	**4.4**	**4.2**	**2.8**	**1.4**	**3.1**
주 유실원인		설비이상 품목교체 대기 자재결품	자재결품 설비이상 설비고장	설비이상 품목교체 설비고장	설비이상 품목교체 소모품교체	설비이상 소모품교체 설비고장	설비이상 소모품교체 설비고장	설비이상 소모품교체 설비고장	설비이상 자재결품 설비고장	설비이상 소모품교체 품질조정	설비이상 설비고장 소모품교체	설비이상 설비고장 공정결품	설비이상 소모품교체 설비고장	

2-3. 시트부문 운영 현황

2-3-1. 매출 및 부가가치 현황

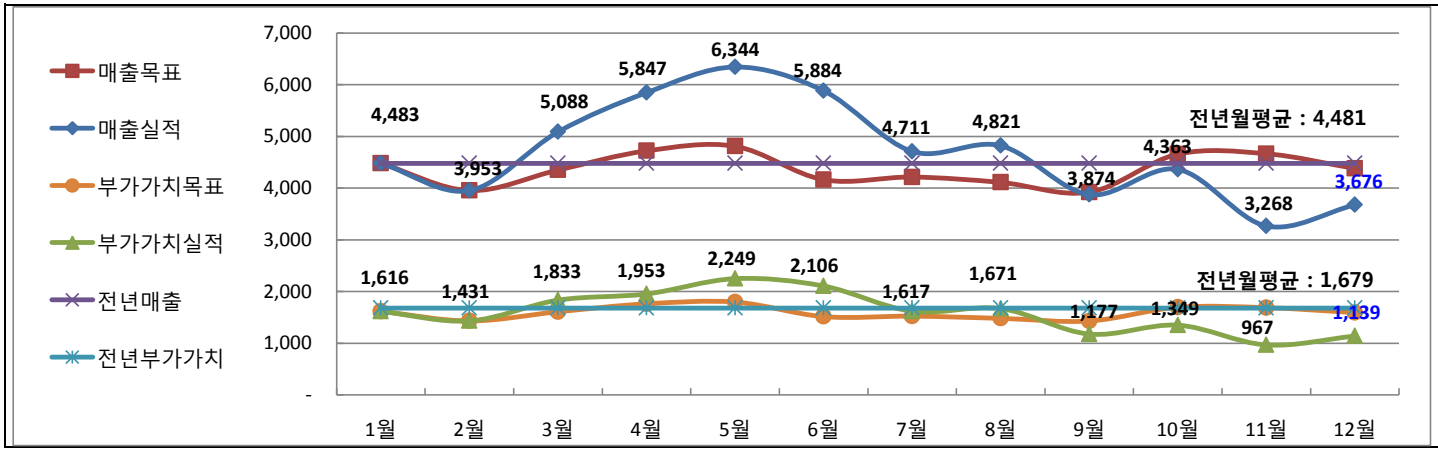

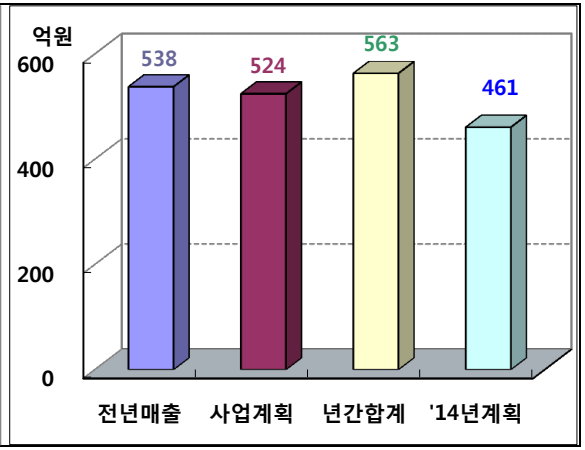

구분			2012년 월평균	2013년 1월	2월	3월	4월	5월	6월	7월	8월	9월	10월	11월	12월	합계	2014년 01월
매출	GMK	계획	1,675	1,802	1,404	1,469	1,400	1,334	1,301	1,278	1,277	1,085	1,329	1,362	1,234	**16,273**	1,260
		실적	1,726	1,802	1,404	1,794	1,852	1,782	1,562	1,154	1,932	1,657	1,485	1,352	1,195	**18,971**	(1,210)
	현대/기아	계획	1,457	1,104	924	1,242	1,367	1,367	1,180	1,242	1,118	1,118	1,304	1,304	1,242	**14,514**	94
		실적	1,348	1,104	924	1,179	1,244	1,523	1,468	1,099	1,038	322	255	239	208	**10,603**	(97)
	수출&기타	계획	1,317	1,577	1,625	1,639	1,955	2,110	1,681	1,696	1,717	1,717	2,025	2,000	1,906	**21,647**	2,126
		실적	1,407	1,577	1,625	2,115	2,751	3,040	2,855	2,457	1,851	1,895	2,624	1,677	2,273	**26,740**	(2,072)
시트사업본부 Total		**계획**	**4,449**	**4,483**	**3,953**	**4,350**	**4,721**	**4,811**	**4,163**	**4,215**	**4,112**	**3,921**	**4,658**	**4,666**	**4,381**	**52,435**	**3,480**
		실적	**4,481**	**4,483**	**3,953**	**5,088**	**5,847**	**6,344**	**5,884**	**4,711**	**4,821**	**3,874**	**4,363**	**3,268**	**3,676**	**56,313**	**(3,378)**
		%	**101%**	**100%**	**100%**	**117%**	**124%**	**132%**	**141%**	**112%**	**117%**	**99%**	**94%**	**70%**	**84%**	**107%**	**(97%)**
부가 가치	GMK	계획	474	461	373	399	381	363	354	348	348	297	363	368	336	**4,390**	344
		실적	478	461	373	474	483	485	431	327	532	453	417	377	325	**5,137**	(332)
	현대/기아	계획	693	594	502	610	671	671	580	610	549	549	641	641	610	**7,227**	34
		실적	647	594	502	604	614	764	720	497	490	120	101	74	71	**5,152**	(30)
	수출&기타	계획	552	561	556	599	710	762	581	565	584	584	691	679	648	**7,521**	644
		실적	554	561	556	755	856	1,000	955	793	649	604	832	516	742	**8,820**	(647)
시트사업본부 Total		**계획**	**1,720**	**1,616**	**1,431**	**1,608**	**1,762**	**1,796**	**1,515**	**1,523**	**1,481**	**1,430**	**1,695**	**1,688**	**1,593**	**19,138**	**1,022**
		실적	**1,679**	**1,616**	**1,431**	**1,833**	**1,953**	**2,249**	**2,106**	**1,617**	**1,671**	**1,177**	**1,349**	**967**	**1,139**	**19,108**	**(1,009)**
		%	**98%**	**100%**	**100%**	**114%**	**111%**	**125%**	**139%**	**106%**	**113%**	**82%**	**80%**	**57%**	**71%**	**100%**	**(99%)**


2-3. 시트부문 운영 현황

2-3-2. 라인 및 인력 운영 현황

라인별		12월 실적 인원	14년 01월 계획						14년 02월 전망				비 고 (충원 및 인력 운영 계획)
			인원	전월대비 증감		Shift	조업일수	O/T	인원	Shift	조업일수	O/T	
				인원	증감율								
전의공장	TRACK ASS'Y	39	37	-2	-5%	1 or 2Shift	20	2T	37	1 or 2Shift	20	2T	C140 Track 라인 2shift
	RECLINER ASS'Y					1 or 2Shift	20	2T		1 or 2Shift	20	2T	C140 Recliner 라인 2shift
	SUB ASS'Y(용접)					1shift	20	2T		1shift	20	2T	
	STAMPING	9	9	0	0%	1Shift	25	2T	9	1Shift	23	2T	
	열처리	5	6	1	20%	1Shift	21	2T	6	1Shift	20	2T	
	전착도장	7	7	0	0%	1Shift	20	2T	7	1Shift	20	2T	
	소계	60	59	-1	-2%				59				9월 66명 / 10월 62명 / 11월 62명
관정공장	TRACK ASS'Y	9	9	0	0%	1Shift	20	2T	9	1Shift	20	2T	
	CORE ASS'Y	5	5	0	0%	1Shift	20		5	1Shift	20		
	수출포장	6	6	0	0%	1Shift	20	2T	6	1Shift	20	2T	
	소계	20	20	0	0%				20				9월 22명 / 10월 23명 / 11월 19명
군산공장	A150, J200, RP	21	21	0	0%	1Shift	20		17	1Shift	20		9월 25명 / 10월 23명 / 11월 21명
인천공장	C140	26	26	0	0%	1Shift	20		26	1Shift	20		9월 31명 / 10월 30명 / 11월 28명
직접 소계		**127**	**126**	**-1**	**-1%**				**122**				**9월 144명 / 10월 138명 / 11월 130명**
간접	생산	5	8	3	60%				8				전의 (1), 전의2 (5), 인천 (2)
	품질/시험	13	13	0	0%				13				전의 (3), 전의2 (5), 군산 (2), 인천 (1), 시험실 (2)
	물류	7	8	1	14%				8				전의 (1), 전의2 (5), 군산 (1), 인천 (1)
	금형/보전	3	6	3	100%				6				금형 (3), 보전 (2), 군산 (1)
	개발	2	3	1	0%				3				시작실 (3)
간접 소계		**30**	**38**	**8**	**27%**				**38**				**9월 30명 / 10월 30명 / 11월 30명**
합계		**157**	**164**	**7**	**4%**				**160**				**9월 174명 / 10월 168명 / 11월 160명**


2-3. 시트부문 운영 현황


2-3-3. 생산성 현황

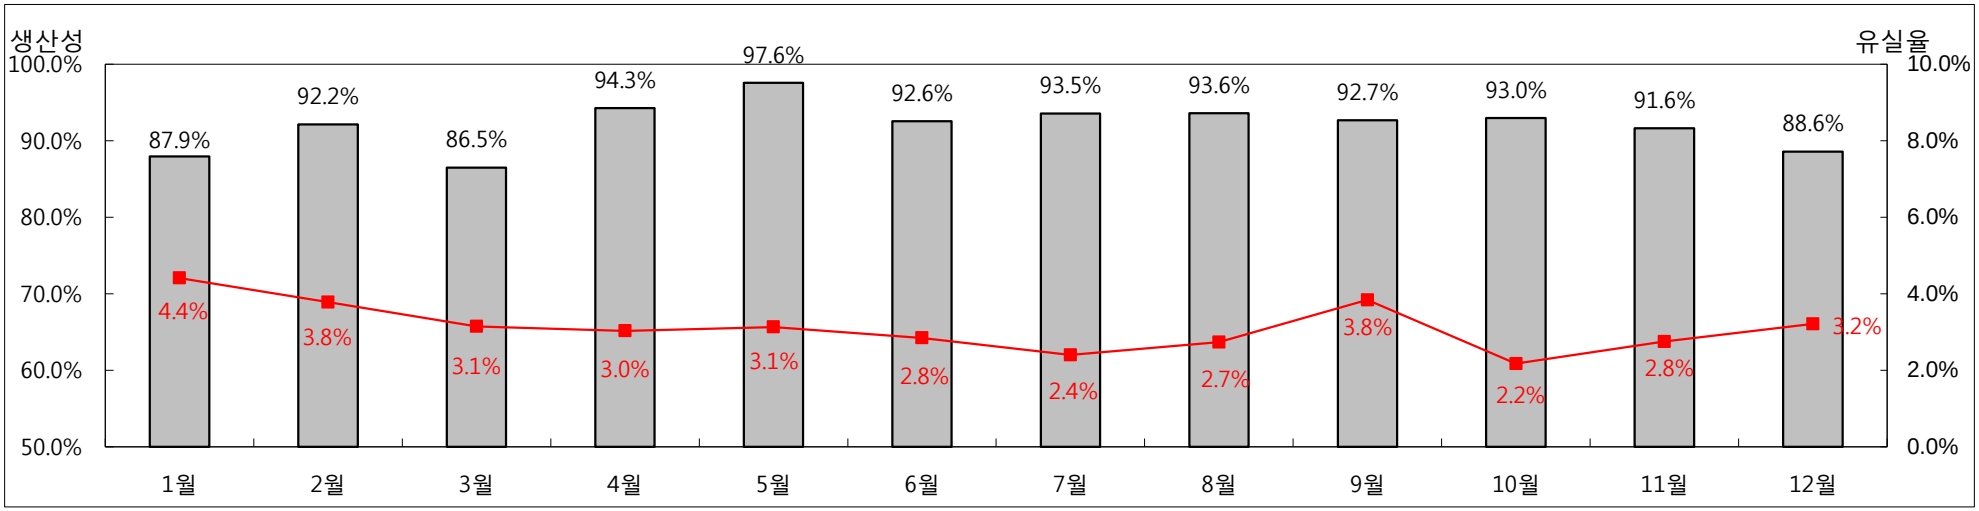

구분	CY2012 실적	CY2013												
		1월	2월	3월	4월	5월	6월	7월	8월	9월	10월	11월	12월	TOTAL
투입공수	391,389	36,969	28,505	37,066	39,020	38,993	36,669	31,486	35,065	21,806	22,408	17,161	20,028	365,177
유실공수	13,315	1,631	1,077	1,166	1,182	1,221	1,044	756	958	837	487	472	643	11,475
작업공수	378,005	35,338	27,428	35,900	37,838	37,772	35,626	30,730	34,107	20,969	21,921	16,689	19,385	353,702
표준공수	346,117	32,510	26,270	32,058	36,780	38,045	33,941	29,454	32,824	20,210	20,833	15,725	17,742	336,392
생산성(%)	88.4%	87.9%	92.2%	86.5%	94.3%	97.6%	92.6%	93.5%	93.6%	92.7%	93.0%	91.6%	88.6%	92.1%
성과율(%)	91.6%	92.0%	95.8%	89.3%	97.2%	100.7%	95.3%	95.8%	96.2%	96.4%	95.0%	94.2%	91.5%	95.1%
유실율(%)	3.4%	4.4%	3.8%	3.1%	3.0%	3.1%	2.8%	2.4%	2.7%	3.8%	2.2%	2.8%	3.2%	3.1%
유실금액(백만원)	240	29	19	21	21	22	19	14	17	15	9	8	12	207
인당 OT	**3.1**	**2.3**	**2.4**	**3.3**	**3.2**	**3.8**	**3.8**	**2.5**	**3.8**	**1.9**	**1.9**	**1.0**	**1.8**	**2.7**
주 유실원인	*설비이상 *REPAIR *자재결품 *품질조정	*설비고장 *REPAIR *자재결품 *품질조정	*REPAIR *설비이상 *자재결품 *품질조정	*REPAIR *품질조정 *설비이상 *금형교환	*설비이상 *품질조정 *REPAIR *금형교환	*설비이상 *품질조정 *REPAIR *금형교환	*품질조정 *REPAIR *설비이상 *금형교환	*품질조정 *REPAIR *금형교환 *설비이상	*품질조정 *REPAIR *금형교환 *설비이상	*REPAIR *금형교환 *설비이상 *자재결품	*금형교환 *REPAIR *금형보수 *설비이상	*금형교환 *금형보수 *REPAIR *설비이상	*REPAIR *금형교환 *금형보수 *설비이상	*REPAIR *설비이상 *품질조정 *금형교환

3. 신규 Porject 진행 및 투자비 현황

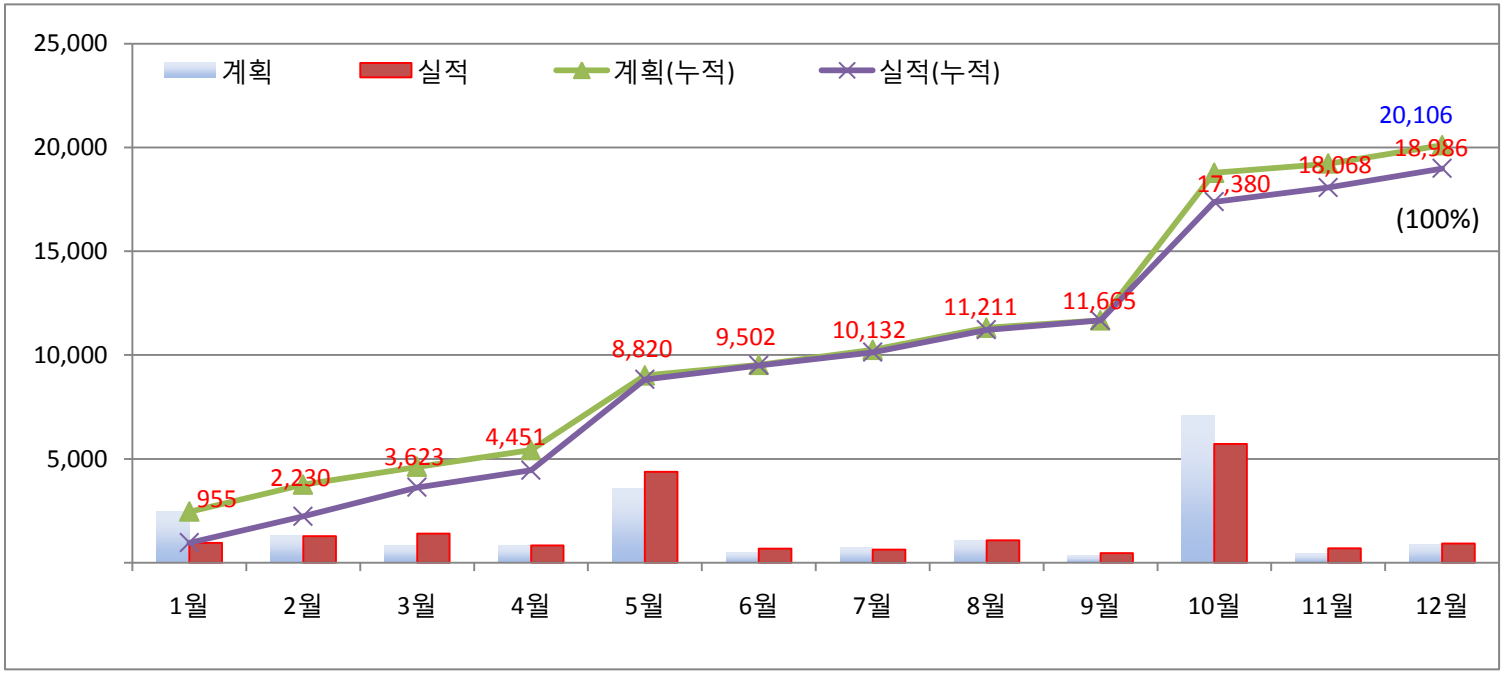

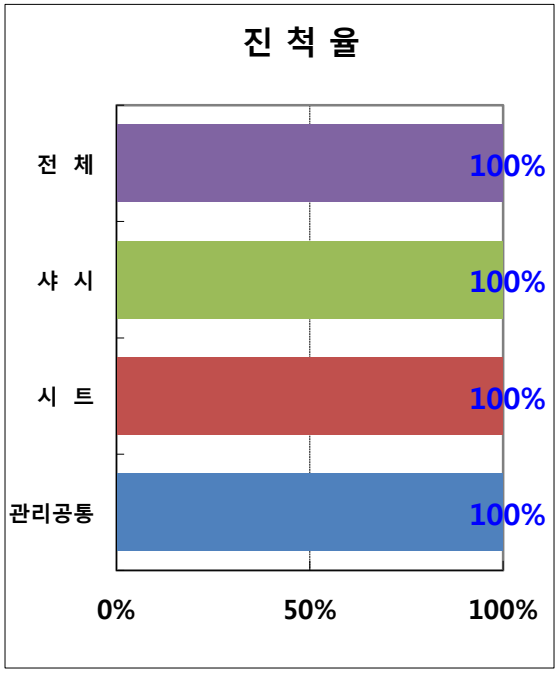

1.사업본부별 투자비 현황

단위:백만원

구분	구분	2012년 실적	2013 투자 계획/실적									절감 금액	미발주
			1Q	2Q	7월	8월	9월	10월	11월	12월	합계		
샤시	계획	18,268	3,020	1,615	315	58	130	4,229	-	526	9,894		-
	실적	17,093	2,405	1,674	222	94	204	4,306	15	526	9,445	449	100%
시트	계획	8,044	1,400	2,986	196	1,000	231	2,814	275	259	9,161		-
	실적	7,681	1,051	3,923	180	979	228	1,354	507	286	8,508	653	100%
관리공통	계획	762	187	312	220	-	-	61	165	107	1,051		-
	실적	702	167	282	228	7	22	55	166	107	1,033	18	100%
합계	계획	27,074	4,608	4,913	731	1,058	361	7,104	440	891	20,106		-
	실적	25,476	3,623	5,879	630	1,079	453	5,715	688	919	18,986	1,120	100%
	%	94%	79%	120%	86%	102%	125%	80%	156%	103%	94%		

구분	회수			합계
	2012년	2013년	2014년	
계획	11,235	11,926	2,863	26,024
실적	11,235	11,917		23,152
계획	3,084	7,742	3,659	14,485
실적	3,084	7,742		10,826
계획				-
실적				-
계획	14,319	19,668	6,522	40,509
실적	14,319	19,659	-	33,978
%	100%	100%		84%

3. 신규 Porject 진행 및 투자비 현황


3-1. 신규 Project 진행 현황-샤시


Legend : ○ (Plan), ● (Finish) , ● (Catch up) , ● Emergency, N.A

Program			Customer	Proto				Production Timing																Remarks
					T.K.O		1st Parts	T.K.O	–			–		–	1st Parts	PPV		V.T.C	MVBns	–	–	MVBs	–	S.O.R.P	
Program	Part Name	Customer	Austem	Design Fix		Tool Off		–	T.K.O	Raw Materail	C/F	Tool Off (Maker T/O)	Ship	Install	–	–	P.V Test		–	PPAP Submit	PPAP App.	–	R @ R	–	
D2UX	Rear C/MBR	SGM	China	N/A	N/A	N/A	N/A	13-12-5	13-2-1	13-5-20	13-6-15	13-6-30	13-11-18	13-11-30	13-12-2	14-1-31	13-12-16	14-5-12	14-5-9	14-5-9	14-6-30	14-7-18	14-8-30	14-10-13	
	Rear Links	SGM	China	N/A	N/A	N/A	N/A	13-3-1	13-2-1	13-5-20	13-6-15	13-6-30	13-11-18	13-1-30	13-12-2	14-1-31	13-12-16	14-5-12	14-5-9	14-5-9	14-6-30	14-7-18	14-8-30	14-10-13	
	Front C/ARM	SGM	China	N/A	N/A	N/A	N/A	13-4-1	13-5-15	13-7-30	13-6-15	13-10-30	13-12-30	14-2-7	13-12-2	14-1-31	14-1-27	14-5-12	14-5-9	14-5-9	14-6-30	14-7-18	14-8-30	14-10-13	
SV71	Podium FS	Futuris	China	Done	Done	Done	Done	13-1-21	13-1-21	13-4-10	13-5-1	13-5-10	13-6-30	13-7-1	13-5-4	13-9-9	TBD	TBD	TBD	14-2-14	14-2-28	14-3-14	14-3-28	14-4-30	고객 일정 조정
D2XX	Rear Axle	SGM	China	N/A	N/A	N/A	N/A	13-4-1	13-4-1	13-5-30	13-6-15	13-7-15	13-8-6	13-8-30	13-9-25	13-10-25	13-9-15	13-1-15	14-1-10	14-1-31	14-2-14	14-2-28	14-4-11	14-6-9	
NGL	F/ LCA	SGM	China	Done	Done	Done	Done	13-8-15	13-8-30	13-10-30	13-10-30	14-1-24	14-4-4	14-4-18	14-5-14	14-7-1	14-6-3	14-9-5	14-9-2	14-10-10	14-10-24	14-11-11	14-11-28	15-1-29	
SGM 358	Rear C/MBR	SGM	China	13-12-27	13-12-30	14-3-7	14-4-3	14-9-18	14-10-3	15-1-1	15-1-1	15-4-23	15-7-20	15-7-30	15-8-26	16-1-25	15-10-11	16-2-28	16-5-2	16-3-28	16-4-15	16-7-11	16-9-10	16-10-27	
	Rear Links	SGM	China	13-12-27	13-12-30	14-3-7	14-3-27	14-9-18	14-10-3	15-1-1	15-1-1	15-4-23	15-7-20	15-7-30	15-8-26	16-1-25	15-10-11	16-2-28	16-5-2	16-3-28	16-4-15	16-7-11	16-9-10	16-10-27	
C1XX /E2XX	Rear C/MBR	SGM	China	N/A	N/A	N/A	N/A	14-6-23	14-7-1	14-9-29	14-9-29	15-1-19	15-4-14	15-5-11	15-6-12	15-8-7	15-6-9	15-10-26	15-10-23	15-11-30	15-12-15	16-1-1	16-2-28	16-4-18	고객일정 미접수
E2XX	Rear Links	GMK	Korea	N/A	N/A	N/A	N/A	14-9-1	14-9-8	14-12-5	14-12-5	15-2-13	N/A	15-3-13	15-4-24	15-5-22	15-5-18	15-8-18	15-8-15	15-9-5	15-9-19	15-10-3	15-12-4	16-2-1	고객일정 미접수
Volvo 315A	FRT Cradle	Volvo	China	N/A	N/A	N/A	N/A	13-9-26	13-9-30	14-1-24	14-2-28	14-4-25	14-9-1	14-9-22	14-5-30	14-6-20	15-7-4	14-10-3	14-11-7	15-1-9	15-1-23	15-2-6	16-2-13	15-3-27	
C14X (FAM B)	FRT Cradle	GMK	Korea	14-12-23	14-12-24	14-2-7	14-2-25	14-4-4	14-4-11	14-7-11	14-7-11	14-11-21	N/A	14-12-26	15-1-23	15-3-27	15-3-27	15-7-31	15-7-24	15-8-28	15-9-11	15-9-25	15-10-30	15-12-31	고객 양산 일정 미접수
M2XX	Steel Wheel	GMK	Austem					12-10-21	12-10-21	13-2-24	N/A	13-2-24	-	-	13-12-11	14-6-27	13-6-10	13-9-10	14-9-12	14-11-10	14-11-20	14-11-21	15-4-10	15-5-2	

3. 신규 Porject 진행 및 투자비 현황

3-2.투자비 현황(발주기준,프로젝트별)-샤시

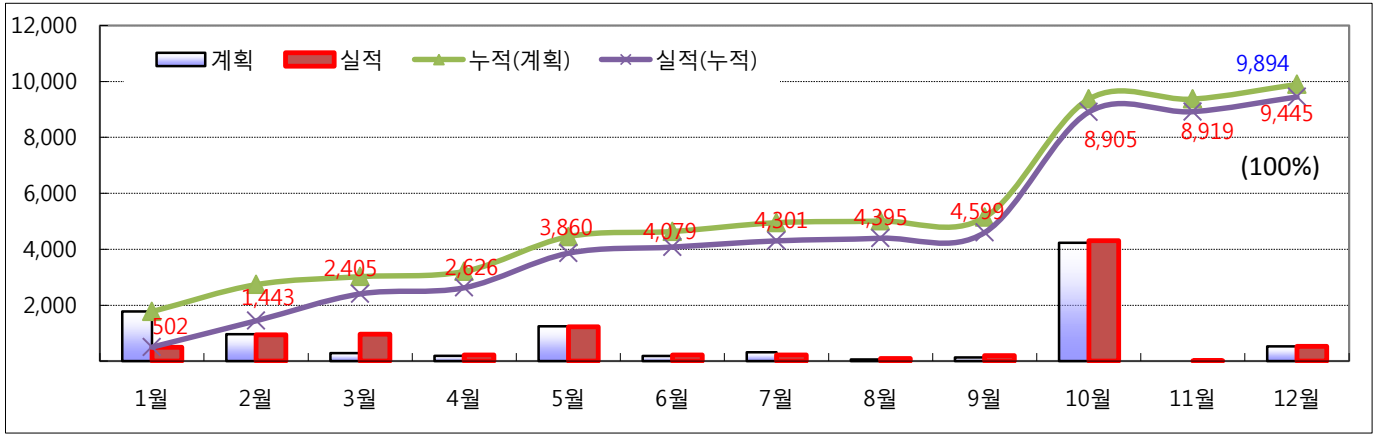

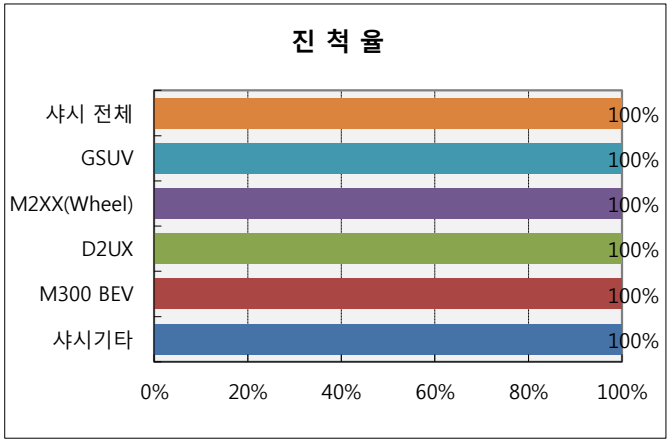

1.프로젝트별 계획/실적


단위:백만원


Project	구분	2012년 실적	2013 투자 계획/실적									절감 금액	미 발주		구분	회수			합계
			1Q	2Q	7월	8월	9월	10월	11월	12월	합계		금액	내용		2012년	2013년	2014년	
GSUV	계획	8,603	1,158	1,360	232	12	50	194	-	90	**3,097**		-		계획	9,027	4,887	2,049	15,963
	실적	8,241	1,185	1,360	155	27	50	194	-	90	**3,061**	36	100%		실적	9,027	4,887		13,914
M2XX(Wheel)	계획	-	631	-	-	-	-	-	-	-	**631**		-		계획			631	631
	실적	-	631	-	-	-	-	-	-	-	**631**	-	100%		실적				
D2UX	계획	634	28	48	-	40	-	-	-	-	**116**		-		계획		345		345
	실적	634	15	48	-	-	40	-	-	-	**103**	13	100%		실적		336		336
M300 BEV	계획	1,561	28	4	-	-	-	-	-	-	**32**		-		계획		3,856		3,856
	실적	1,147	28	4	-	-	-	-	-	-	**31**	0	100%		실적		3,856		3,856
샤시기타	계획	7,470	1,175	203	83	6	80	4,035	-	436	**6,018**		-		계획	2,208	2,838	183	5,229
	실적	7,071	546	263	67	67	114	4,112	15	436	**5,618**	400	100%		실적	2,208	2,838		5,046
합계	계획	18,268	3,020	1,615	315	58	130	4,229	-	526	**9,894**		-		계획	11,235	11,926	2,863	26,024
	실적	17,093	2,405	1,674	222	94	204	4,306	15	526	**9,445**	449	100%		실적	11,235	11,917		23,152
	%	94%	80%	104%	70%	161%	157%	102%		100%	**95%**				%	100%	100%		89%

2.특기 사항

3. 신규 Porject 진행 및 투자비 현황

3-3.해외법인 先투자비 현황(발주기준,프로젝트별)-Pos-austem(Kunshan)

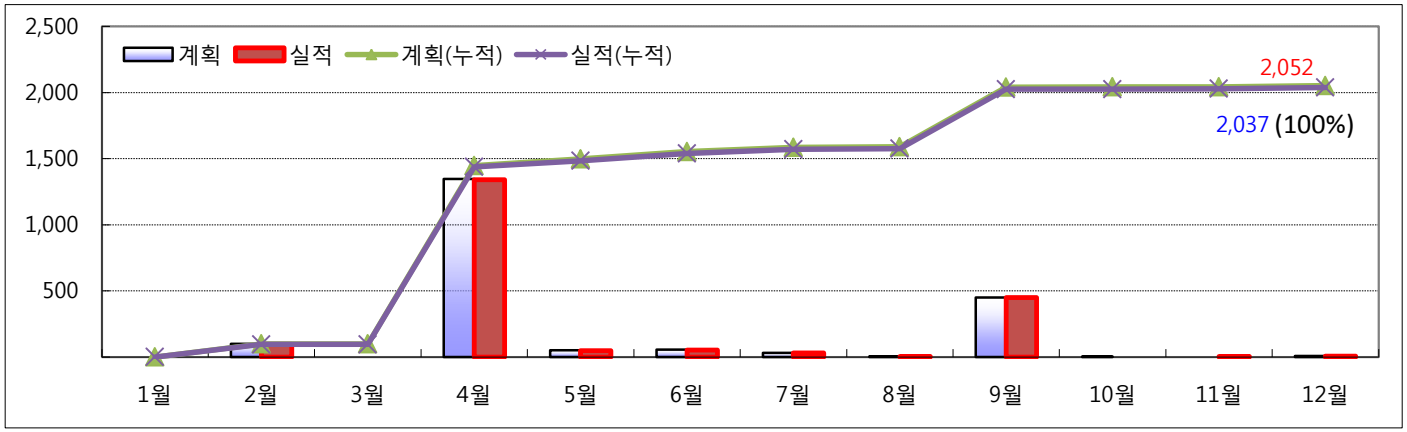

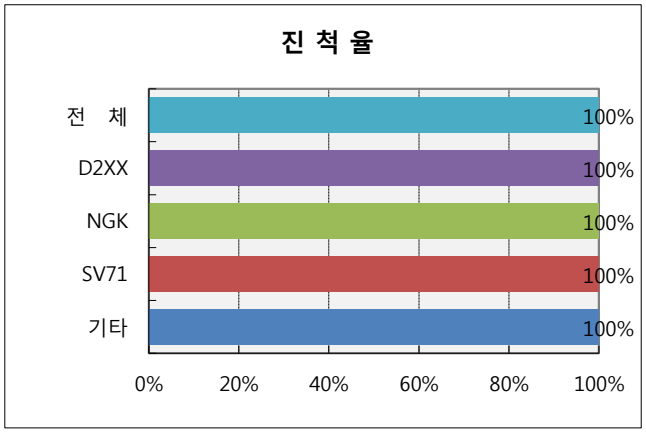

1.프로젝트별 계획/실적

단위:백만원


Project	구분	2012년 실적	2013 투자 계획/실적								합계	절감 금액	미 발주	
			1Q	2Q	7월	8월	9월	10월	11월	12월			금액	내용
D2XX	계획	275	-	89	-	5	-	-	-	-	**94**	-	-	
	실적	275	-	85	1	5	-	-	-	-	**91**	3	100%	
NGK	계획	99	8	-	-	-	450	4	-	5	**467**	-	-	
	실적	99	8	-	-	-	450	-	4	5	**467**	-	100%	
SV71	계획	-	-	1,240	-	-	-	-	-	-	**1,240**	-	-	
	실적	-	-	1,232	-	-	-	-	-	-	**1,232**	7	100%	
GSUV	계획	-	-	-	-	-	-	-	-	3	**3**	-	-	
	실적	-	-	-	-	-	-	-	-	3	**3**	-	100%	
기타	계획	224	91	125	31	-	-	-	-	-	**248**	-	-	
	실적	221	88	125	31	-	-	-	-	-	**243**	4	100%	
합계	계획	598	100	1,454	31	5	450	4	-	8	**2,052**	-	-	
	실적	594	96	1,443	32	5	450	-	4	8	**2,037**	14	100%	
	%	99%	96%	99%	102%	100%	100%	0%		100%	**99%**			


구분	회수			합계
	2012년	2013년	2014년	
계획	-	443		443
실적	-	398		398
계획	-	-	489	489
실적	-	-		-
계획	-	1,755		1,755
실적	-	1,755		1,755
계획	3,198			3,198
실적	3,198			3,198
계획	654	351		1,005
실적	654	351		1,005
계획	3,852	2,549	489	6,890
실적	3,852	2,504		6,356
%	100%	98%		92%

2.특기 사항

3. 신규 Porject 진행 및 투자비 현황

3-3.해외법인 先투자비 현황(발주기준,프로젝트별)-Pos-austem(Yantai)

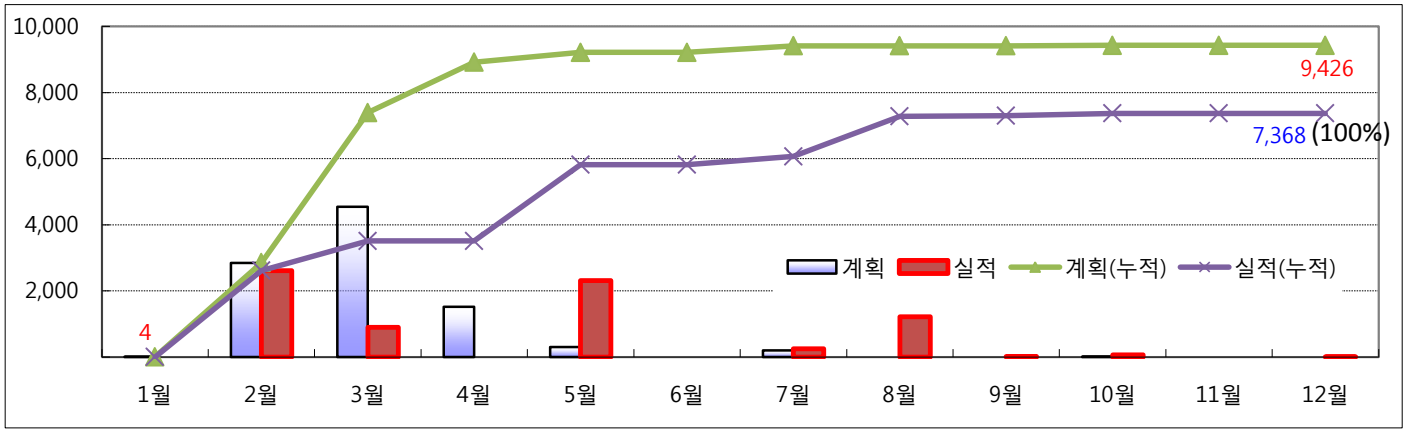

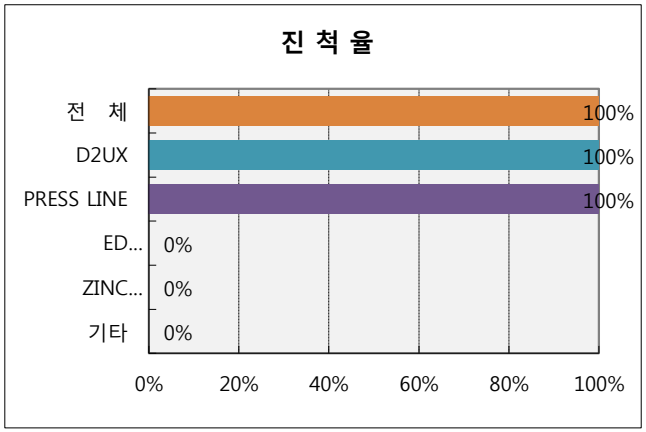

1.프로젝트별 계획/실적


단위:백만원


Project	구분	2012년 실적	2013 투자 계획/실적									절감 금액	미 발주		구분	회수			합계
			1Q	2Q	7월	8월	9월	10월	11월	12월	합계		금액	내용		2013년	2014년	2015년	
D2UX	계획	-	7,393	1,821	-	-	-	12	-	-	**9,226**	-	-		계획	4,210	4,651		8,861
	실적	-	3,509	2,231	246	1,215	-	67	-	1	**7,269**	1,957	100%		실적	4,210			4,210
PRESS LINE	계획	4,300	-	-	200	-	-	-	-	-	**200**	-	-		계획	1,435	3,350		4,785
	실적	4,300	-	79	-	-	19	-	-	-	**98**	102	100%		실적	1,435			1,435
ED COATING	계획	-	-	-	-	-	-	-	-	-	**-**	-		Pos-austem	계획	-			-
	실적	-	-	-	-	-	-	-	-	-	**-**	-		직접투자	실적	-			-
ZINC COATING	계획	-	-	-	-	-	-	-	-	-	**-**	-		Magni Coating	계획	-			-
	실적	-	-	-	-	-	-	-	-	-	**-**	-		직접투자	실적	-			-
기타	계획	-	-	-	-	-	-	-	-	-	**-**	-	-		계획	-			-
	실적	-	-	-	-	-	-	-	-	-	**-**	-			실적	-			-
합계	계획	4,300	7,393	1,821	200	-	-	12	-	-	9,426	-	-		계획	5,645	8,001	-	13,646
	실적	4,300	3,509	2,310	246	1,215	19	67			7,368	2,059	100%		실적	5,645			5,645
	%	100%	100%	127%	123%			560%			78%				%	100%			41%

2.특기 사항

3. 신규 Porject 진행 및 투자비 현황

3-3.해외법인 先투자비 현황(발주기준,프로젝트별)-O'zauto austem

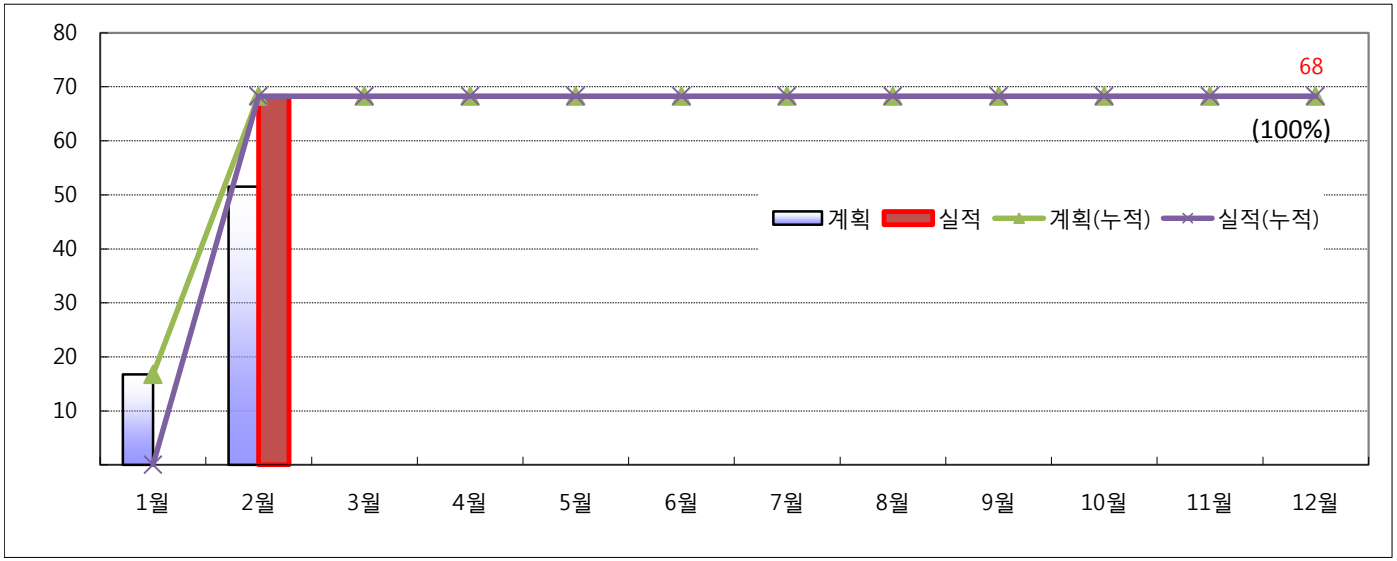

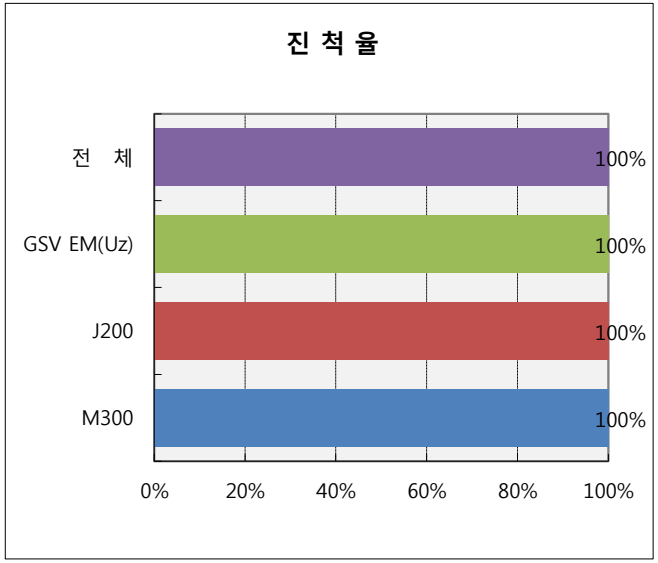

1.프로젝트별 계획/실적

단위:백만원

Project	구분	2012년 실적	2013 투자 계획/실적									절감 금액	미 발주		구분	회수			합계
			1Q	2Q	7월	8월	9월	10월	11월	12월	합계		금액	내용		2012년	2013년	2014년	
GSV EM(Uz)	계획	920	23	-	-	-	-	-	-	-	**23**		-		계획	25,693			25,693
	실적	920	23	-	-	-	-	-	-	-	**23**	-			실적	23,329	2,363		25,693
J200	계획	24	46	-	-	-	-	-	-	-	**46**		-		계획	2,858			2,858
	실적	24	46	-	-	-	-	-	-	-	**46**	-			실적	2,568	211		2,779
M300	계획	7	-	-	-	-	-	-	-	-	**-**		-		계획	856			856
	실적	7	-	-	-	-	-	-	-	-	**-**	-			실적	428	428		856
합계	계획	951	68	-	-	-	-	-	-	-	68		-		계획	29,407	-		29,407
	실적	951	68	-	-	-	-				68	-	100%		실적	26,325	3,002		29,327
	%	100%	100%	0%	0%	0%	0%				100%				%	89.5%			99.7%

2.특기사항

1)LEMAX T.A 일부 미회수(79백만원)

3. 신규 Porject 진행 및 투자비 현황


3-4. 신규 Project 진행 현황-시트


Legend : ○ (Plan), ● (Finish) , ● (Catch up) ,● Emergency, N.A

Division	Program	Item	Region	Customer	Award	Proto	—		T.K.O	—			—	—		—	—	MVBns (yy/mh/dy)	—	MVBs		S.O.R.P	REMARK
				Austem	—		D.V Test	V.T.C	—	T.K.O	Raw Material	C/F	Tool Off	Install	P.V Test	V.T.C	PPAP Submit	—	PPAP Approval	—	R @ R	—	
Seat	**GSUV**	Recliner	Korea	GMK	13-8-20					13-10-23		13-12-10	13-12-20	13-12-30	14-2-5		14-3-10		14-3-30		14-3-20	2013-04-01	설비 입고 TRY
	L43/L38	Manual - Track	KOREA	JCDS						**13-01-30**		13-03-15	13-04-30	13-08-10	13-10-30		13-11/20		13-11-30			13-12-02	양산대응중
		Power - Track	KOREA	JCDS						**13-01-30**		13-03-15	13-04-30	13-08-10	13-10-30		13-11/20		13-11-30			13-12-02	양산대응중
	M2xx	Track	N/A	GMK	12-03-29	12-10-15	**13-02-10**			13-08-27			13-01-30	14-02-20	14-04-30		14-12-20		14-01-30			15-02-10	C-SPEC TKO 11/08
		Recliner	N/A	GMK	12-03-29	12-10-15	**13-02-10**			13-08-27			13-01-30	14-02-20	14-04-30		14-12-20		14-01-30			15-02-10	C-SPEC TKO 11/08
		Height Adjuster	N/A	GMK	12-03-29	12-10-15	**13-02-10**			13-08-27			13-01-30	14-02-20	14-04-30		14-12-20		14-01-30			15-02-10	C-SPEC TKO 11/08

3. 신규 Porject 진행 및 투자비 현황

3-5.투자비 현황(발주기준,프로젝트별)-시트

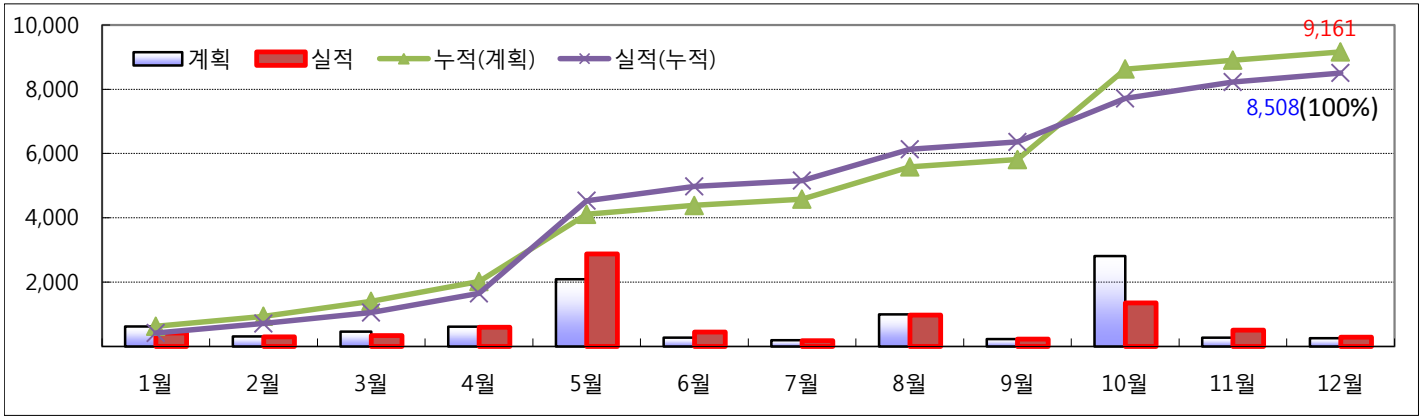

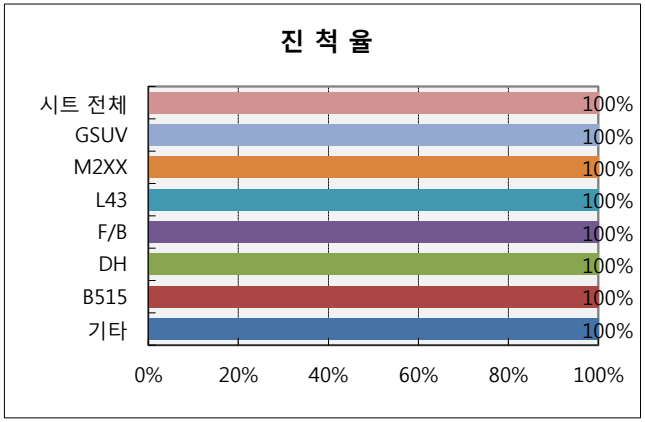

1.프로젝트별 계획/실적


단위:백만원


Project	구분	2012년 실적	2013 투자 계획/실적									절감 금액	미 발주	
			1Q	2Q	7월	8월	9월	10월	11월	12월	합계		금액	내용
T300/GSUV	계획							1,600	78	20	**1,698**		-	
	실적							1,180	280	48	**1,508**	190	100%	
M2XX	계획	554	732	150	17	892	3	1,193	45	51	**3,083**		-	
	실적	554	718	1,050	17	892	3	113	45	51	**2,889**	194	100%	
L43	계획	1,096	60	2,166	14	66	67	10	32	125	**2,540**		-	
	실적	960	60	2,086	31	66	67	10	32	125	**2,477**	62	100%	
F/B	계획	305	20	58	2	7					**87**		-	
	실적	305	20	58	2	7					**87**	0	100%	
DH	계획	713	85	195			46			36	**362**		-	
	실적	635	25	255			46			36	**362**	0	100%	
B515	계획	966	91	249	68		112		20	19	**557**		-	
	실적	954	47	284	68	9	112		20	19	**557**	0	100%	
기타	계획	4,409	412	169	95	35	4	12	100	8	**834**		-	
	실적	4,271	182	190	62	5		52	130	8	**628**	206	100%	
합계	계획	8,044	1,400	2,986	196	1,000	231	2,814	275	259	**9,161**		-	
	실적	7,681	1,051	3,923	180	979	228	1,354	507	286	**8,508**	653	100%	
	%	95%	75%	131%	92%	98%	98%	48%	184%	111%	**93%**			

구분	회수			합계
	2012년	2013년	2014년	
계획			543	543
실적				
계획			3,026	3,026
실적				
계획				
실적				
계획				
실적				
계획		7,632		7,632
실적		7,632		7,632
계획	809	110		919
실적	809	110		919
계획	2,275		90	2,365
실적	2,275			2,275
계획	3,084	7,742	3,659	14,485
실적	3,084	7,742		10,826
%	100%	100%		75%

4. TCR2013 원가절감 현황

단위:백만원

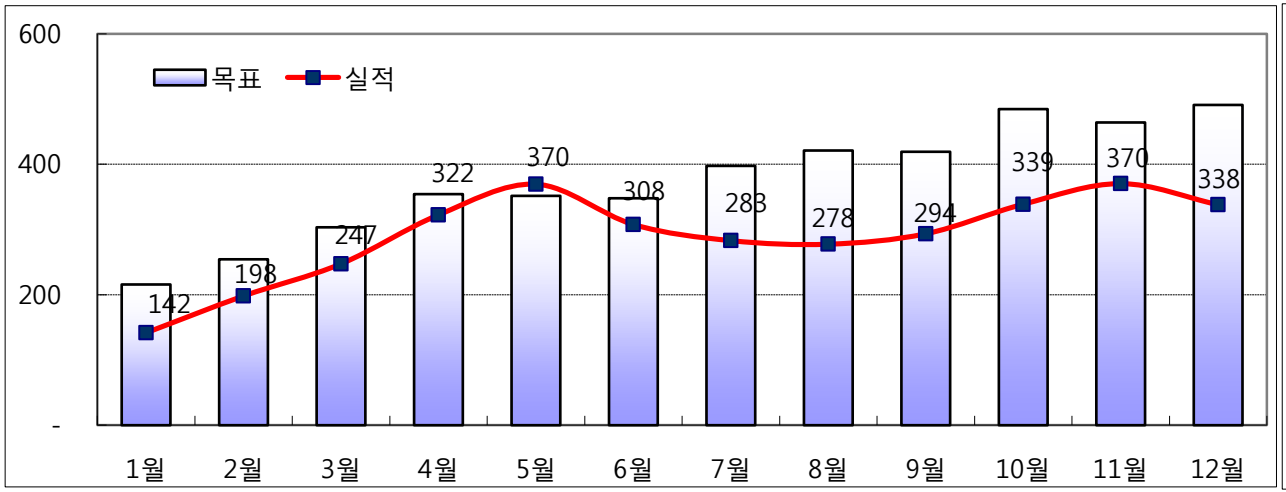


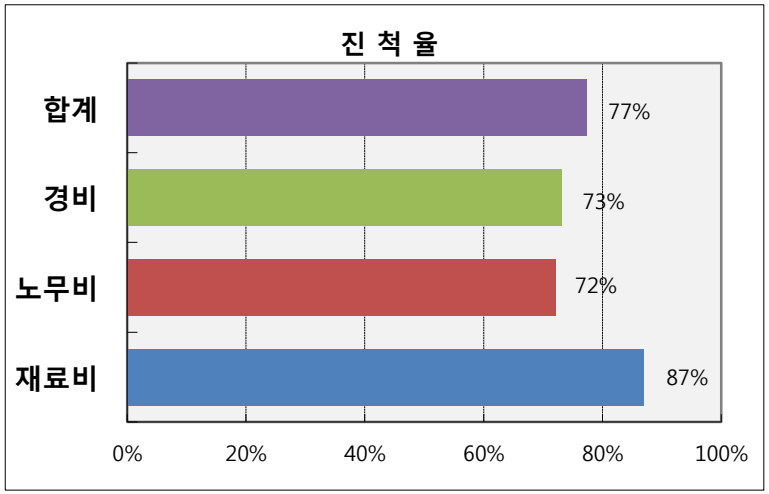


구분		전년실적	1월	2월	3월	4월	5월	6월	7월	8월	9월	10월	11월	12월	누계	합계
재료비	목표	3,519	86	97	110	122	122	115	117	135	133	167	154	165	1,522	1,522
	실적	4,612	84	76	85	100	121	124	100	94	96	148	160	136	1,323	1,323
	%	131%	99%	78%	77%	82%	99%	108%	85%	69%	72%	89%	104%	82%	87%	87%
노무비	목표	2,679	56	77	95	130	128	127	146	154	155	181	177	193	1,620	1,620
	실적	2,109	27	64	99	110	113	105	115	93	97	98	108	137	1,168	1,168
	%	79%	49%	83%	104%	85%	88%	83%	79%	60%	63%	54%	61%	71%	72%	72%
경비	목표	1,304	74	80	99	102	102	106	135	131	131	137	134	133	1,363	1,363
	실적	1,129	30	58	64	112	135	78	69	90	100	93	102	65	997	997
	%	87%	40%	73%	65%	109%	133%	74%	51%	69%	76%	68%	77%	49%	73%	73%
합계	**목표**	**7,502**	**216**	**254**	**303**	**354**	**352**	**348**	**398**	**421**	**419**	**485**	**464**	**491**	**4,506**	**4,506**
	실적	**7,850**	**142**	**198**	**247**	**322**	**370**	**308**	**283**	**278**	**294**	**339**	**370**	**338**	**3,488**	**3,488**
	%	**105%**	**66%**	**78%**	**82%**	**91%**	**105%**	**88%**	**71%**	**66%**	**70%**	**70%**	**80%**	**69%**	**77%**	**77%**

특기사항

5. 2013년 고객사 차량판매 실적 현황

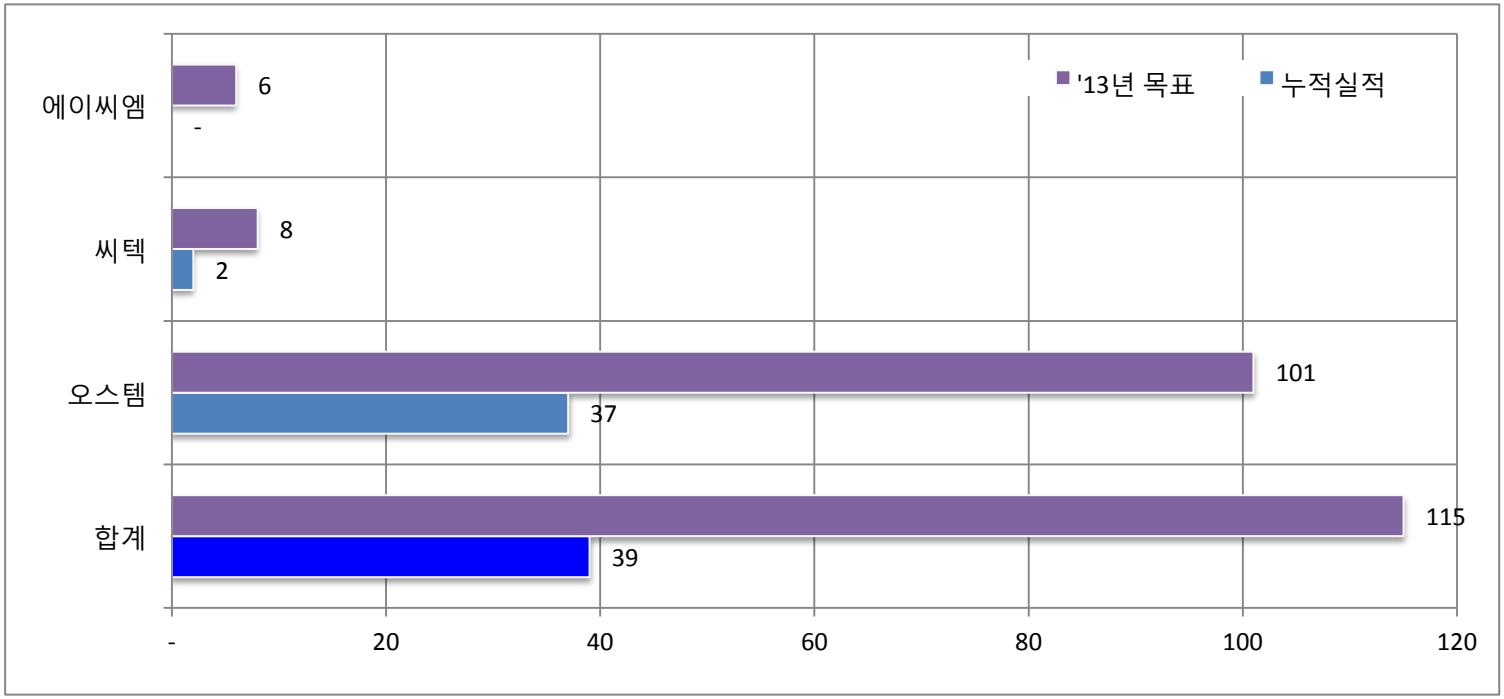

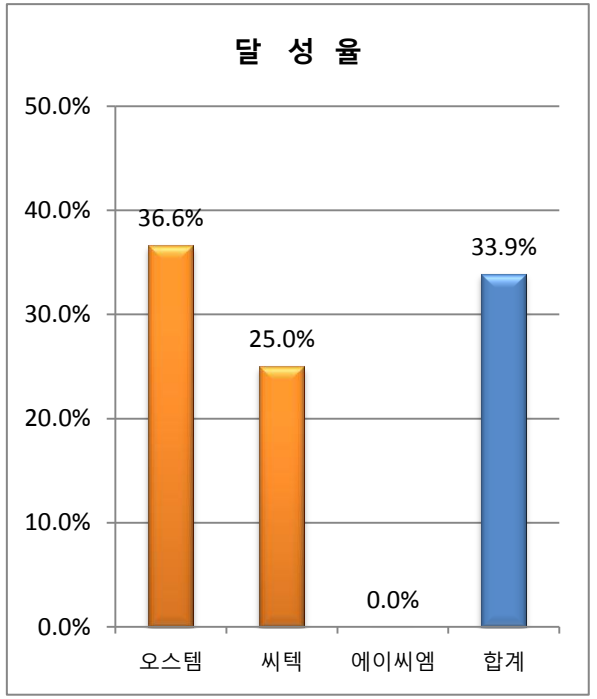

구분	'12년 현황			'13년 목표	2013년 월별 차량 판매 현황												누계(~12월)		비고
	목표	실적	달성율		1월	2월	3월	4월	5월	6월	7월	8월	9월	10월	11월	12월	실적	달성율	
합계	**97**	**63**	**65%**	**115**	**2**	**3**	**5**	**4**	**8**	**2**	**3**	**4**	**1**	**3**	**1**	**3**	**39**	**33.9%**	
오스템	85	58	68%	**101**	2	2	5	4	8	2	3	4	1	3	-	3	37	36.6%	
씨텍	7	4	57%	**8**	-	1	-	-	-	-	-	-	-	-	1	-	2	25.0%	
에이씨엠	5	1	20%	**6**	-	-	-	-	-	-	-	-	-	-	-	-	-	0.0%	

강평말씀
